



Capital Projects Report
to the
Citizens' Bond Oversight Committee

March 7, 2023

TABLE OF CONTENTS

Overview of Projects

Aerial View.....Page 1

Project Status Reports – Projects in Initial Start-Up, Planning & Design

Athletics Stadium and Fields Project.....Page 2

Palm Springs Development Project.....Page 3

Roadrunner Motors (Automotive Technology Training Center).....Page 4

Science Building Renovation Project.....Page 5

Project Status Reports – Current Construction Projects

Coachella Chelsea Property Tenant Improvement.....Page 6

Indio Campus Expansion – New Building and Site Development.....Page 7

Indio Campus Expansion - Renovation.....Page 8

Indio Child Development Center.....Page 9

Financial Review

Project Budgets.....Pages 10-15



AERIAL

Projects in Programming & Design

- 1 Athletics Stadium and Fields Project
- 2 Science Building Renovation Project
- 3 Palm Springs Development Project
- 4 Roadrunner Motors (Automotive Technology Training Center)

Projects in Construction

- 5 Indio Campus Expansion/Renovation
- 6 Indio Child Development Center
- 7 Coachella Chelsea Property Tenant Improvement



Palm Desert Campus



Indio Campus



Palm Springs Development Project



Coachella Chelsea Property



**Roadrunner Motors
(Automotive Technology Training
Center)**

ATHLETICS STADIUM AND FIELDS PROJECT

DESIGN

Project Description

The Athletics Facilities Feasibility study was completed in 2020, and identified a menu of options, which were prioritized and assembled into proposed phases. This phase will demolish the existing football stadium and construct a new 20,000 sf stadium building which will house team locker rooms and associated auxiliary spaces, a 3,000 sf weight room, sports official facilities, and support areas including equipment storage rooms, laundry, video, and IT rooms. In addition, the project will install new sports lighting at both the football and soccer fields and create landscaped new and renovated parking.

Project Data

Project Manager: Larry Moen
 Design Professional: SGH Architects
 Pre-Construction Manager: W.E. O'Neil Construction Company
 Primary Funding Source: Measure CC Funds
 Project Size : 390,000 SF (Buildings & Land)
 Project Address: 43500 Monterey Avenue, Palm Desert, CA 92260

Project Update

- Construction Documents in progress
- Initial DSA submission accepted
- Full DSA submission end of January 2023




Stadium Entrance




Football Stadium

Estimated Project Timeline

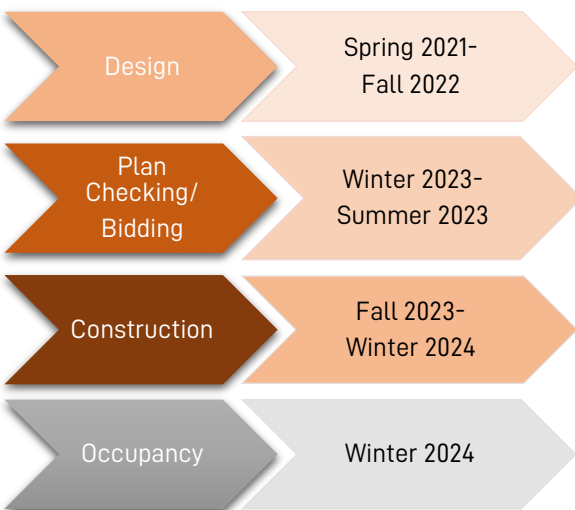

Total Budget: \$36,475,740 Construction Budget: \$23,200,000

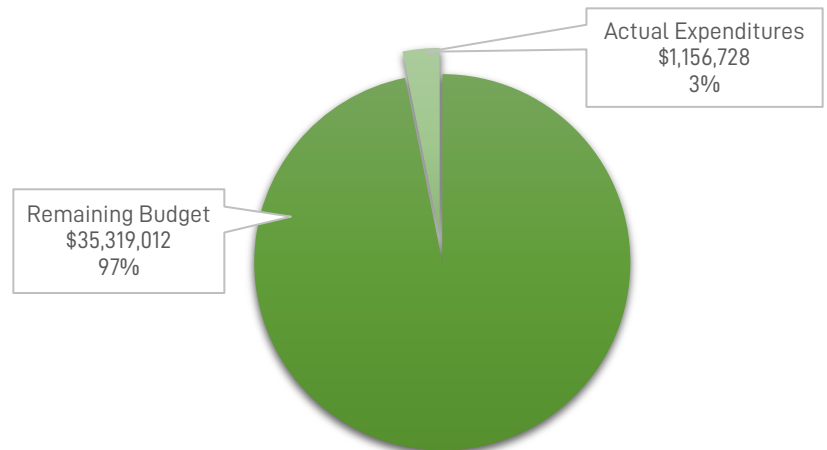

PALM SPRINGS DEVELOPMENT PROJECT

DESIGN

Project Description


The planning and development of a new campus on approximately 27 acres of reclaimed land in Palm Springs. The campus will accommodate a combination of traditional instruction methodologies and hands-on technical education. Informed by industry partners and local stakeholders, the campus will establish and augment signature programs including Hospitality and Culinary Arts, Digital Media and Media Production, Radio, Health, and Sustainable Technologies. To accommodate these programs, Phase 1 of the project includes construction of an education Accelerator containing flexible classrooms, meeting spaces, student services, maker spaces, and high-tech learning laboratories. Future phases on the 27-acre site have yet to be decided.



Aerial of Site

Project Data

Project Manager: Robert Rauscher
 Design Professional: WRNS Studio
 Construction Manager: TBD
 Primary Funding Source: Measure CC Funds
 Project Size: Phase 1 = estimated 142,646 GSF
 Project Budget: Phase 1 = estimated \$290,000,000
 Project Address: 2363 Tahquitz Canyon Way, Palm Springs, CA 92262
 Purchase Cost of Site: \$24,050,299.74
 Purchase Date of Site: 2018

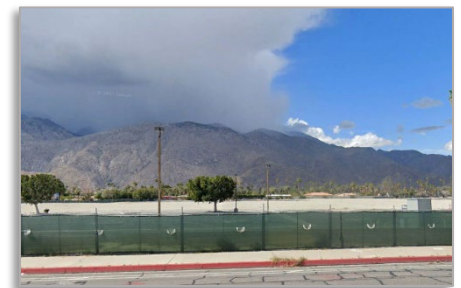


Existing Undeveloped Site


Project Update – Phase 1

- Stakeholder and Advisory Group meetings were completed in December 2022
- Schematic Design will be completed with a presentation by the project architect to the Board of Trustees at their January 2023 meeting
- Current Cost Estimates are in line with the project budget, within an industry-standard tolerance of 3%

Estimated Project Timeline – Phase 1

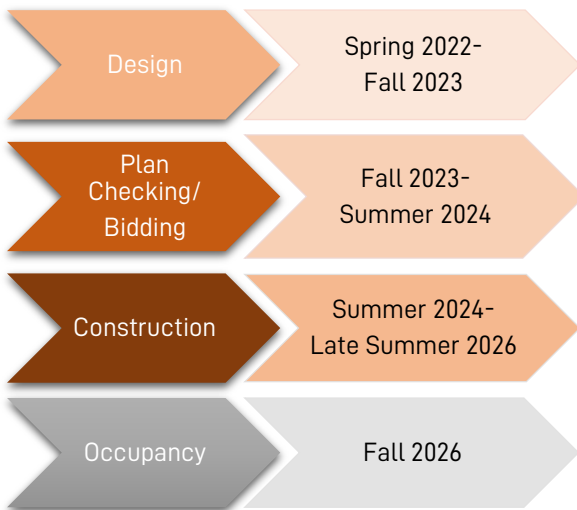

Total Budget: \$345,390,589

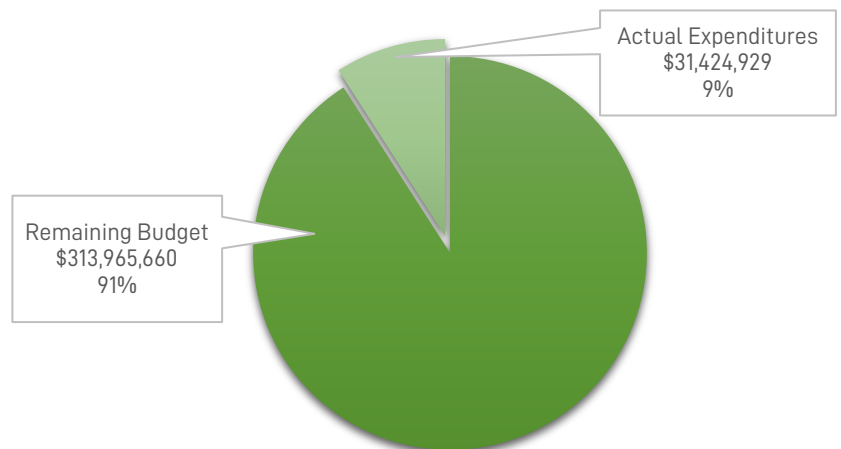

ROADRUNNER MOTORS (AUTOMOTIVE TECHNOLOGY TRAINING CENTER)

DESIGN

Project Description

The new Automotive Technology Training Center facility will be constructed on a 5.8 acre parcel in Cathedral City, and will provide specialized and generalized classrooms, teaching laboratories including service vehicle bays/lifts, offices, conference room, support space, and parking. The initial effort involved programming, site planning, and schematic design.

Project Data

Project Manager: Keith Martinez

Design Professional: Marlene Imirzian & Associates Architects

Preconstruction Services: Ledesma & Meyers Construction Company, Inc.

Primary Funding Source: Measure CC

Project Size: 25,983 GSF

Project Address: 67893 and 67905 East Palm Canyon Drive, Cathedral City, CA 92234

Purchase Cost of Site: \$3,050,000.00

Purchase Date of Site: September 2019



Main Entrance




Interior Lift Gallery


Project Update

- Design Development Phase in progress

Estimated Project Timeline

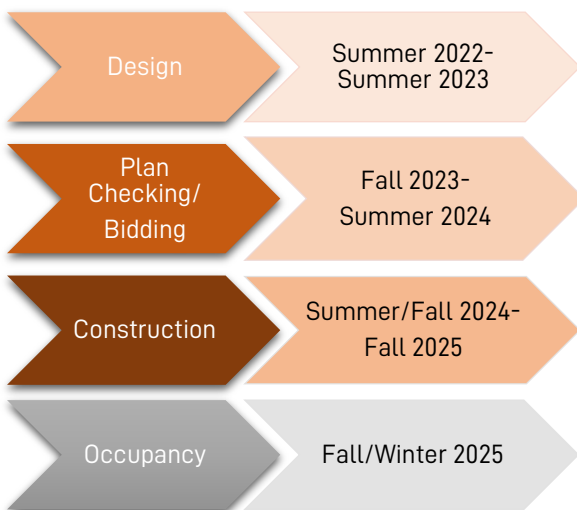

Total Budget: \$37,750,000 Construction Budget: \$21,750,000

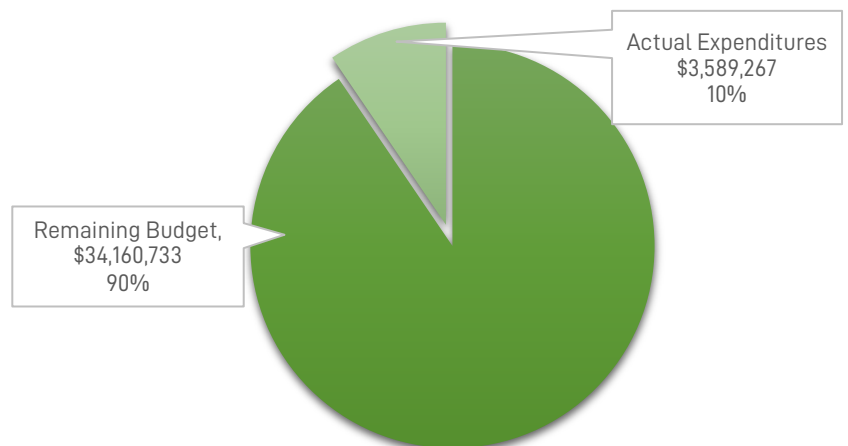

SCIENCE BUILDING RENOVATION PROJECT

DESIGN

Project Description

The project scope includes the interior renovation and modernization of the Science Building, originally built in the early 1960's and partially upgraded in 2002. Located on the College's Palm Desert campus, it is part of the campus's core complex of "historic" buildings. The intent is to preserve the original exterior architecture of the building while upgrading its structure and services to meet current codes. The existing building is approximately 15,025 gsf in size, of which 10,150 sf is considered assignable space. The project's current scope of work will require the demolition of the interior with a complete interior remodel providing new laboratory and classroom spaces with the latest technology, finishes and lighting, all providing an enhanced instruction experience. Building support spaces, laboratory services and new staff offices will also be included with an efficient layout connected by minimal circulation/hall space to maximize space efficiency. The remodel will also include the replacement of all utilities including, but not limited to the electrical, plumbing, and mechanical systems, including new exhaust systems for the laboratory hoods. A new roof will be provided as part of the minimal Exterior improvements.



South Elevation



East Elevation

Project Data

Project Manager: Keith Martinez

Design Professional: Gensler

Construction Manager: TBD

Primary Funding Sources: Measure CC/State Funding


Project Size: 15,025 GSF

Project Address: 43500 Monterey Avenue, Palm Desert, CA 92260


Project Update

- Design Development Phase in progress
- DSA approval expected early Winter 2023

Estimated Project Timeline

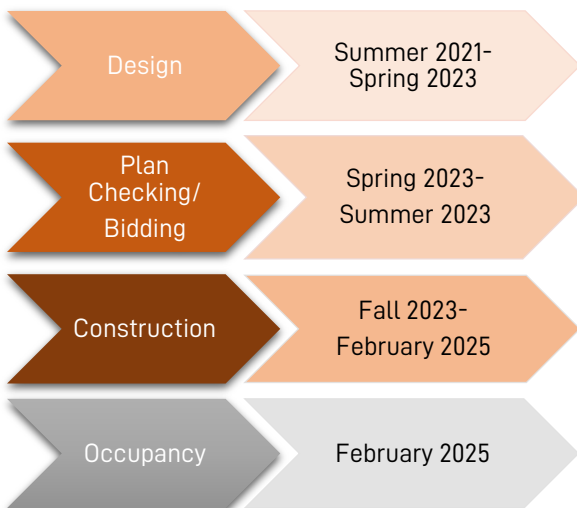

Total Budget: \$15,400,000 **Construction Budget: \$11,255,000**

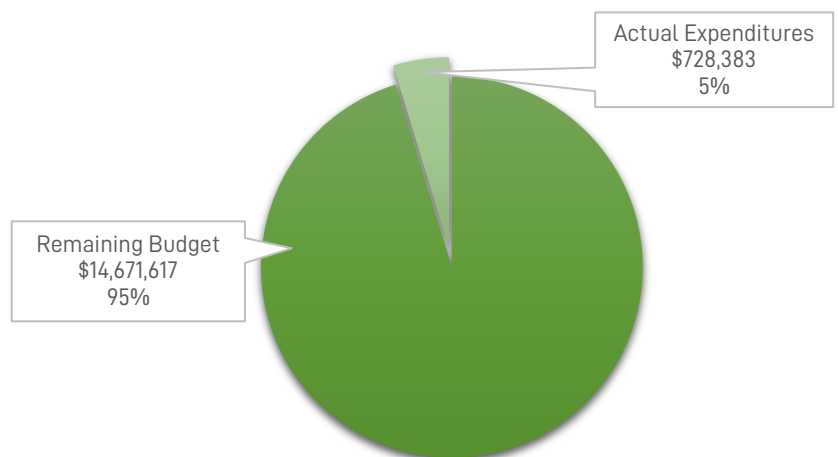


COACHELLA CHELSEA PROPERTY TENANT IMPROVEMENT

CONSTRUCTION

Project Description

Tenant improvement of leased space in the heart of Coachella. The commercial units (#10 and #20 of Pueblo Viejo Villas) will be the new location for Student Services, which is currently temporarily located in the old Coachella Library. The 1,366 sf space is a "Cold Dark Shell" which requires full improvements including, but not limited to, framing and drywall installations, HVAC, fire alarm and sprinklers, interior paint, new flooring, acoustical ceiling, lighting, electrical alterations, data, and communication. The finished space will have two (2) single occupancy restrooms, two (2) offices, a Greeter's station, a computer lab with open workstations and a tutorial workshop space with systems furniture and audiovisual equipment.



Student Work Spaces

Project Data

Project Manager: Keith Martinez
 Design Professional: SGH Architects
 Construction Manager: N/A
 Primary Funding Source: RDA Funds
 Project Size : 1,366 GSF
 Project Address: 1279 6th Street, Coachella, CA 92236




Faculty/Staff Office Space

Project Update


- Construction completed December 30, 2022
- Punch Walk week of January 9, 2023
- COD IT computer installation January 2023

Estimated Project Timeline

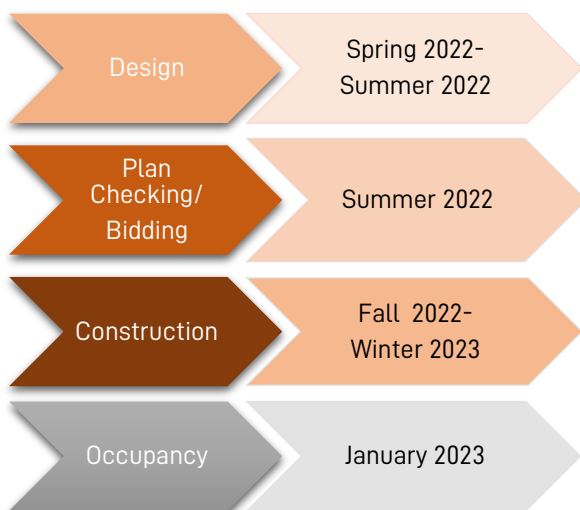

Total Budget: \$667,000

Construction Budget: \$412,000

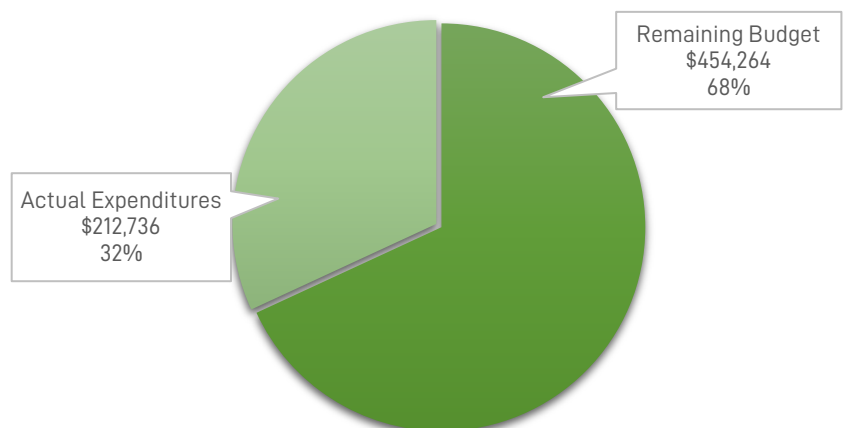


INDIO CAMPUS EXPANSION – NEW BUILDING AND SITE DEVELOPMENT


CONSTRUCTION

Project Description

The expansion of College of the Desert's Indio Campus extends the campus site north of the existing building with the addition of a new 67,000 sf building, and site enhancements that include a new shade structure and flexible outdoor space between the buildings. The new building includes an enlarged Student Success Center, Public Safety facilities and Student Health Offices. It will significantly expand the instructional facilities with new classrooms, science laboratories, lecture halls, computer labs and a Maker Space, expanded faculty office space, a student dining commons and study spaces. The building will also have the necessary support and circulation spaces for maintenance of the Indio Campus, various informal social spaces along corridors, and a large outdoor deck space on the third level. Site improvements include parking lots, landscape buffers, and vehicular circulation for the new enlarged campus extents.

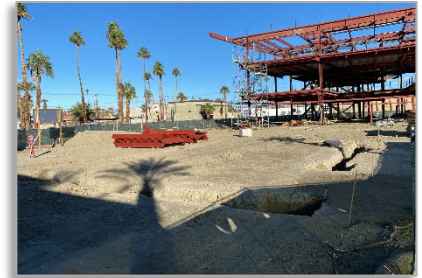

Looking North from Existing Building

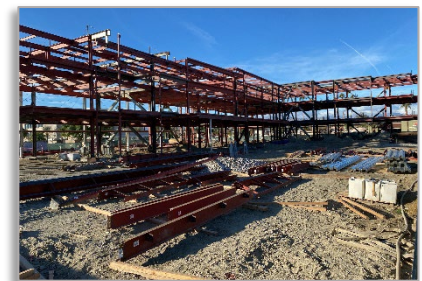

North Side of New Building

Project Data

Project Manager: Ryan Lamb
 Design Professional: HMC Architects
 Construction Manager: Tilden-Coil Constructors
 Primary Funding Source: Measure CC
 Project Size: 67,000 GSF
 Project Address: 45524 Oasis St., Indio, CA 92201

Project Update


- Notice of Default, Termination and Demand for Performance on Bond has been issued to the Steel Contractor for breach of contract
- Bond Office is working with the Contractor's Surety and District Legal Counsel to expedite the transition to a new contractor
- Working with Surety to minimize delays
- Construction Manager re-sequencing work & developing revised schedule options to minimize delays
- Site grading and concrete pours for grade beams in progress
- Site utility connections at street in progress

Estimated Project Timeline



***Total Budget: \$73,825,000**

***Construction Budget: \$42,400,000**

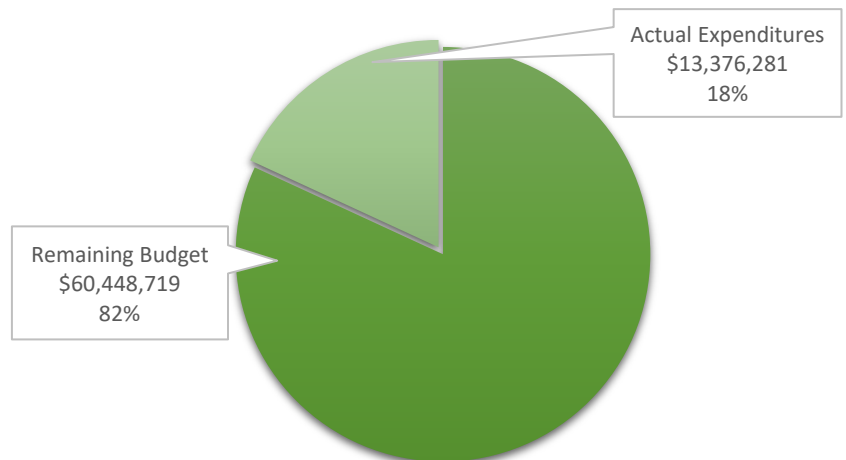

INDIO CAMPUS EXPANSION - RENOVATION

CONSTRUCTION

Project Description

The expansion of College of the Desert's Indio Campus includes 10,000 sf of renovations to the existing building. Renovations include the removal of various campus level functions that are to be rehoused in the new building, the enclosure of the breezeway, and the conversion of the newly available spaces into additional instructional and student study spaces. Site improvements have included the removal of the temporary modular classroom buildings and resurfacing that portion of the parking lot.

Project Data

Project Manager: Ryan Lamb
 Design Professional: HMC Architects
 Construction Manager: Tilden-Coil Constructors
 Primary Funding Source: Measure CC
 Project Size: 10,000 GSF
 Project Address: 45524 Oasis St., Indio, CA 92201

Project Update

- Construction will start following completion of the new building (Approximately Winter 2024)




Lobby Renovation & Cyber Lab



Perforated Metal at New Lobby

Estimated Project Timeline

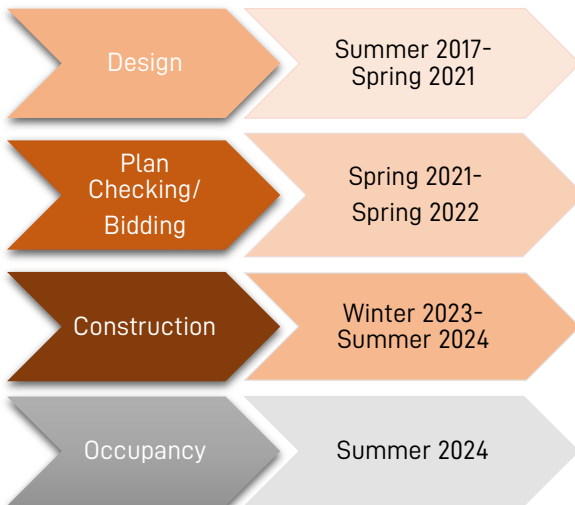

***For budget information see Indio Expansion – New Building and Site Development**

INDIO CHILD DEVELOPMENT CENTER

CONSTRUCTION

Project Description

The Child Development Center at College of the Desert's Indio Campus extends the campus site south of the existing building with the addition of a new 18,000 sf building and approximately 7,000 sf of Play Yards with shade structures. The new building will include toddler & preschool classrooms, 2 of each, and support spaces required for a state of the art child care facility, meeting State Chancellor's guidelines. The building will also house an adult ECE classroom and observation spaces. Site improvements include undergrounding of existing overhead utilities, demolition of existing structures and new parking lots.

Project Data

Project Manager: Ryan Lamb
 Design Professional: HMC Architects
 Construction Manager: Erickson-Hall Construction Co.
 Primary Funding Source: Measure CC
 Project Size : 18,169 GSF
 Project Address: 45742 Oasis St., Indio, CA 92201



Looking North Toward Playground Courtyard




CDE Classroom Interior


Project Update

- Roofing and framing ongoing
- Mechanical, Electrical and Plumbing rough-ins in progress
- Shade structure and walk-way canopy erection in progress
- Alley and Under-sidewalk electrical infrastructure work pending
- Encroachment Permit approval by City

Estimated Project Timeline

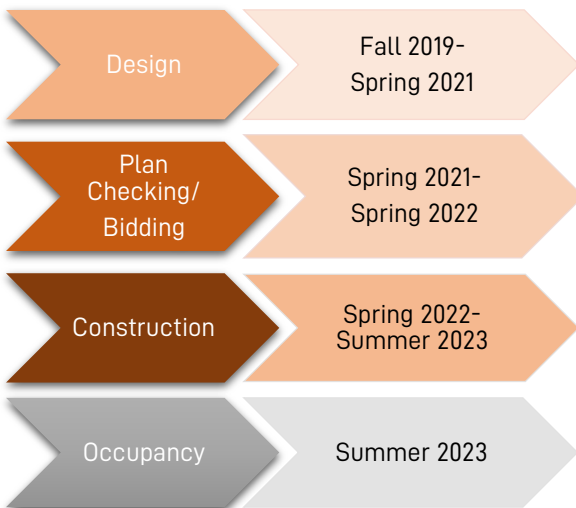

Total Budget: \$26,185,000 Construction Budget: \$13,693,000

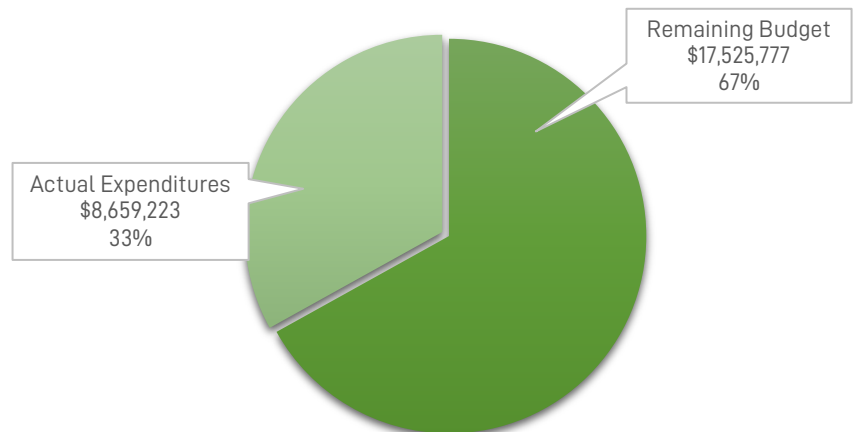

Active Projects

Project Name	Budget	Actual Expenditures (as of 12.31.2022)			Remaining Budget
		Measure B	Measure CC	Non-Bond	
ADA Transition Plan	\$484,935	\$0		\$394,422	\$90,513
Ag Canopy	\$174,000	\$0		\$113,650	\$60,350
Applied Sciences Canopy	\$481,300	\$0		\$465,952	\$15,348
Athletics Stadium and Fields	\$36,475,740	\$0	\$1,049,988	\$106,740	\$35,319,012
Building C Landscape Renovation	\$95,000	\$0		\$67,187	\$27,813
CDC Internal Wall	\$6,000	\$0		\$5,900	\$100
CDC Outdoor Lavatories	\$44,000	\$0		\$42,010	\$1,990
CSSC Restroom Door Automation	\$10,000	\$0		\$9,097	\$903
Campus Electronic Sign	\$300,000	\$20,891		\$0	\$279,109
Campus Energy Monitoring	\$295,801	\$0		\$289,570	\$6,231
Campus Signage Standards	\$30,500	\$0		\$9,845	\$20,655
Coachella Chelsea Property T.I.	\$667,000	\$0		\$212,736	\$454,264
Cravens 269	\$65,000	\$0		\$56,783	\$8,217
Deferred Maintenance – Access Controls	\$900,000	\$0		\$24,209	\$875,791
Deferred Maintenance – Central Plan Towers	\$798,000	\$0		\$6,199	\$791,801
Deferred Maintenance - FACP	\$598,000	\$0		\$497,905	\$100,095
Deferred Maintenance - HVAC Package Units	\$536,000	\$0		\$377,574	\$158,426
Deferred Maintenance - MAL Towers	\$350,000	\$0		\$287,146	\$62,854
ECE Shade Structures	\$116,600	\$0		\$18,109	\$98,491
Gates and Bollards	\$189,000	\$0		\$161,637	\$27,363
HILB Site Modifications	\$96,000	\$0		\$75,704	\$20,296
HILB and C Building	\$34,477,444	\$4,334,859	\$28,277,080	\$250	\$1,865,255
Indio Bookstore Remodel	\$208,000	\$0		\$34,722	\$173,278
Indio CDC	\$26,185,000		\$7,885,152	\$774,071	\$17,525,777
Indio Campus Expansion	\$73,825,000	\$603,002	\$12,716,325	\$56,954	\$60,448,719
Indio Modulars	\$858,030	\$0		\$841,213	\$16,817
Indio Modulars #2	\$945,000	\$0		\$922,584	\$22,416
Infrastructure Upgrade - Ph III	\$11,732,136	\$11,082,594		\$647,042	\$2,500
McCallum Theater Asphalt Replacement	\$1,727,000	\$0	\$2,404	\$77,150	\$1,647,446
Mecca/Thermal Campus	\$26,308,991	\$102,597		\$0	\$26,206,394
Music Classroom Acoustics	\$92,300	\$0		\$63,317	\$28,983
North Annex Two	\$997,000	\$0		\$896,137	\$100,863
Old Coachella Library	\$88,000	\$0		\$85,449	\$2,551
Old Warehouse Renovation	\$957,582	\$0		\$956,284	\$1,298
PSD Office Remodel	\$59,000	\$0		\$48,755	\$10,245
PaCE Furniture	\$304,059	\$0		\$267,211	\$36,848
Palm Springs Development Project	\$345,390,589	\$19,647,456	\$8,579,894	\$3,197,579	\$313,965,660
Palm Springs Modulars	\$7,010,000	\$5,111,070	\$464,415	\$1,302,850	\$131,665
Pollock Theater	\$50,000	\$0		\$41,900	\$8,100
Quad Sculpture	\$815,000	\$0		\$25,500	\$789,500
RDA Small Maintenance Projects	\$3,783,207	\$0		\$3,508,048	\$275,159
Roadrunner Motors	\$37,750,000	\$3,049,219	\$326,148	\$213,900	\$34,160,733
S/A Maker Space	\$27,000	\$0		\$21,566	\$5,434
Science Building Renovation	\$15,400,000	\$0	\$249,615	\$478,768	\$14,671,617
South Annex Assessment Testing	\$146,000	\$0		\$74,699	\$71,301
South/East Annex	\$6,137,300	\$0		\$6,098,514	\$38,786
TOTAL ACTIVE PROJECTS	\$637,986,514	\$43,951,688	\$59,551,021	\$23,856,838	\$510,626,967

Completed Projects (as of 12.31.2022)

Project Name	Completion Date	Final Cost
Adjunct Faculty Office Renovation	Oct 2017	\$966,211
Admin. Bld. Conf. Rm	May 2020	\$254,270
Admin. Toilet Rm. Reconfiguration	Mar 2019	\$181,320
Administration Building	Jun 2018	\$47,647
Ag Science Project	Aug 2010	\$105,804
Alumni Centre	Jun 2009	\$2,714,816
Applied Sciences	Dec 2014	\$12,125,867
Applied Sciences Solar Yard	Aug 2017	\$43,223
Aquatics Swimming Pool Demolition	Oct 2008	\$310,103
Art 100 Renovation	Sep 2019	\$401,864
ASCOD Offices	Jun 2019	\$120,277
Athletic Facilities	Apr 2015	\$21,476,803
Athletics Precinct Master Plan - Phase I	May 2014	\$20,432
Barker Nursing Complex	Mar 2009	\$10,973,913
Baseball Scoreboard	Oct 2007	\$77,711
BEEPS Salad Bar	Jan 2018	\$51,641
Berger Faculty Innovation Center	Aug 2015	\$349,000
Black Student Success Center	Apr 2020	\$32,953
Bond Office Modular	Oct 2020	\$462,815
Burn Tower	Mar 2009	\$2,875,267
Business Building Renovation	Jan 2010	\$4,598,036
Campus IT Infrastructure	Jun 2013	\$2,498,904
Campus Standards & Design	Jul 2006	\$615,343
Career & Workforce Solutions Center	May 2016	\$299,875
Carol Meier Hall 1 & 4	Aug 2016	\$145,999
Carol Meier Lecture Hall Roof Repair	Jun 2007	\$317,728
CDC Re-Roof	Aug 2019	\$57,487
CDC Shade Structures	Oct 2019	\$142,645
CDC/ECE Laundry	Jun 2020	\$37,393
Central Annex Village	Feb 2007	\$2,308,330
Central Campus Quad Renovation	May 2020	\$4,258,903
Central Campus Redevelopment - Legacy	May 2018	\$1,808,503
Central Plant	Jan 2010	\$13,127,485
Central Plant MBCx	Sep 2013	\$3,335,803
Central Plant Renovation	Apr 2019	\$1,253,410
Child Development Center	Dec 2014	\$6,066,890
Child Development Center Outdoor Lab	Aug 2018	\$709,679
Classroom Utilization Study	Nov 2018	\$42,000



Barker Nursing Complex



Central Campus Quad Renovation



Early Childhood Development Center

Completed Projects (continued)

Project Name	Completion Date	Final Cost
Communication Building	Dec 2014	\$20,258,662
Contractor Lay Down Area	Apr 2007	\$724,890
Cravens Student Services Center	Apr 2010	\$22,954,847
CSSC 2nd Floor Wall Opening	Aug 2016	\$4,864
CSSC Second Floor Renovation	Jan 2014	\$148,060
CSSC Vet. Ctr. Furniture	Jan 2019	\$15,405
Culinary Kitchen	Jul 2007	\$410,529
Date Palm Removal	Nov 2004	\$311,447
Demo Central Annex / Cooling Tower	Dec 2014	\$336,262
Desert Energy Enterprise Center	Sep 2016	\$14,220
Desert Hot Springs	Aug 2009	\$1,140
Desert Hot Springs Campus Renovation	Jun 2017	\$691,635
Diesel Mechanics Flooring	Apr 2007	\$14,154
Diesel Mechanics Lifts	Aug 2017	\$7,500
Dining Facility Renovation	Jun 2010	\$5,399,910
Dream Center	May 2020	\$390,453
ECE Build Back / Fire Repairs	Jun 2021	\$1,539,763
Facilities Yard Improvements	Jul 2010	\$416,825
Foundation Office Furniture	May 2020	\$57,757
Fred Waring Entrance Paving	Sep 2020	\$238,925
Friends of The Library	Dec 2019	\$120,391
Golf Academy Lighting Improvements	Aug 2011	\$119,113
Golf Ball Screening	Jan 2010	\$64,663
Gym Concessions Room 3 Remodel	Aug 2015	\$8,451
Gymnasium Quick Start Repairs	Mar 2007	\$144,679
Imaging	Jun 2013	\$399,540
Indio Campus	Feb 2015	\$24,123,997
Indio Campus Retail Space/Classroom	Jan 2018	\$1,589,125
Indio Student Kiosk	Mar 2018	\$925,398
Infrastructure Upgrade - Ph I	Aug 2009	\$14,512,593
Infrastructure Upgrade - Ph II	Dec 2009	\$11,727,628
Institutional Effectiveness Renovation	Aug 2016	\$243,369
KCOD Antenna	Jan 2019	\$16,084
KCOD Radio Station	Aug 2018	\$192,104
LA-13 Computer Lab	Jan 2018	\$35,463
M1 Renovation	May 2019	\$125,028
M2	Jul 2016	\$118,495



Communication Building



Cravens Student Services Center



Indio Campus

Completed Projects (continued)

Project Name	Completion Date	Final Cost
Math Science Technology Center	Jul 2013	\$24,303,698
Mecca/Thermal Campus Expansion & Lab Redesign	Aug 2016	\$3,440,913
Mecca-Thermal Interim Modulars	Mar 2009	\$9,913,929
Mecca-Thermal Septic Sewer System	Aug 2012	\$288,401
Monterey Entrance	Sep 2014	\$5,417,239
Monterey Wall & Landscaping	Sep 2007	\$1,544,946
MSTC Renovation	Mar 2019	\$85,782
Music Building Interior Storage	Feb 2017	\$16,516
Music Building Shade Structure Demo	Feb 2017	\$52,000
Nursing Building Renovation	Aug 2010	\$3,538,287
Nursing Building Rm.10	Aug 2018	\$125,741
Old Art Building Renovation	Mar 2017	\$332,997
Palm Springs - Demolition (Jack in the Box)	Jun 2021	\$675,888
Palm Springs - Demolition (Mall)	Aug 2020	\$3,773,488
Palm Springs - Preliminary Site Work	May 2022	\$122,135
Parking Lot Improvement	Dec 2015	\$286,588
Parking Ticket Machines	Sep 2016	\$81,324
Pavement Removal North Alumni Road	Sep 2007	\$28,721
Practice Fields Lighting Improvements	Jan 2011	\$266,772
Prop 39 - Year 1 RCX	Aug 2014	\$343,194
Prop 39 - Year 2	Mar 2015	\$355,300
Prop 39 - Year 3	Aug 2016	\$241,432
Prop 39 - Year 4 and Year 5	Jun 2019	\$656,987
PSA Parking & Mag. Falls Entrance	May 2010	\$949,794
PSA ROOM 16	Aug 2017	\$228,621
Public Safety Academy	Nov 2009	\$14,917,722
Relocations	Sep 2018	\$568,049
Road Repair	Jun 2016	\$480,247
Safety/Security Improvements CDC & AR	Jun 2007	\$256,377
Scene Shop	Sep 2007	\$75,654
Science Labs	Dec 2007	\$223,624
Second Floor Diesel Mechanics Renovation	Aug 2017	\$703,992
Security Cameras & Emergency Phones	Apr 2012	\$132,450
Sidewalk Repairs	Aug 2006	\$38,846
Site Remediation	Sep 2018	\$318,301
Soccer Field Lighting	Feb 2008	\$57,449
Sociology Classroom Furniture	Jan 2019	\$142,293



Math Science Technology Center



Monterey Entrance



Public Safety Academy

Completed Projects (continued)

Project Name	Completion Date	Final Cost
Softball Field Lighting	Aug 2020	\$790,524
Softball Stadium	Dec 2007	\$1,093,803
Solar Photovoltaic System	Jan 2014	\$14,022,190
South Annex - HR Renovation	Jun 2017	\$106,871
South Annex 13 Remodel	Aug 2016	\$54,815
South Annex 3 & 8 Remodel	Aug 2016	\$72,024
South Annex Ph I	Sep 2008	\$273,569
South Annex Ph II	Feb 2009	\$1,027,825
South Annex Ph III - DSPS Modulares	Jun 2010	\$646,294
South Annex Tenant Improvement	Mar 2016	\$39,127
South Parking Lot	Oct 2007	\$1,004,767
South/North Annex Ph I Classroom Modulares	Jun 2008	\$1,920,155
Stadium Showers & Lockers	Jun 2006	\$37,187
Stagecraft Shop	Dec 2014	\$2,042,836
Storm Drain Outlet Structure	Jan 2009	\$1,563,111
Telephone Systems / VOIP Upgrade Ph I	Sep 2008	\$964,487
Temporary Access Road	Nov 2007	\$87,252
Temporary Dining Facility	Aug 2009	\$752,840
Transfer Center Renovation	May 2020	\$424,066
Velma Dawson House Lot	Dec 2007	\$27,500
Visual Arts Building	Jul 2014	\$8,434,163
Visual Arts Canopy	Aug 2016	\$194,258
Visual Arts Kiln Building Demo	Apr 2010	\$179,079
Wayfinding	Oct 2014	\$473,684
Wayfinding - Phase 2	Jul 2015	\$197,543
Weatherproofing	Jun 2016	\$459,990
Weight/Training Rooms	Mar 2012	\$1,255,138
Western Parking Lot	Apr 2008	\$2,564,965
Western Parking Lot Landscaping	Nov 2007	\$266,422
Wireless Access Project	Apr 2008	\$322,555
WVC Palm Springs Campus - Legacy	Apr 2018	\$5,927,213
TOTAL COMPLETED PROJECTS		\$325,831,662



Solar Photovoltaic System



Stagecraft Shop



Visual Arts Building

Future Projects

Project Name	Estimated Budget	Allocation to Date (as of 12.31.2022)		
		Measure B	Measure CC	Non-Bond
West Valley Desert Hot Springs Ph II	\$2,500,000	\$0	\$0	\$0
TOTAL FUTURE PROJECTS	\$2,500,000	\$0	\$0	\$0

Summary

Project Status	Budget	Actual Expenditures (as of 12.31.2022)				Remaining Budget
		Measure B	Measure B Interest/Refinance Income	Measure CC	Non-Bond	
Active Projects	\$637,986,514	\$43,951,688	\$0	\$59,551,021	\$23,856,838	\$510,626,967
Completed Projects	\$325,831,662	\$267,140,869	\$11,215,000	\$8,767,949	\$38,707,844	\$0
Auxiliary Operations	\$62,147,554	\$35,407,443	\$0	\$18,168,178	\$937,863	\$7,634,070
TOTAL SUMMARY	\$1,025,965,730	\$346,500,000	\$11,215,000	\$86,487,148	\$63,502,545	\$518,261,037

